

SED-279


SoCalGas Response to SED Data Request 89

Well-25 Schematic

I.19-06-016

ALJs: Hecht/Poirier

Date Served: May 3, 2021

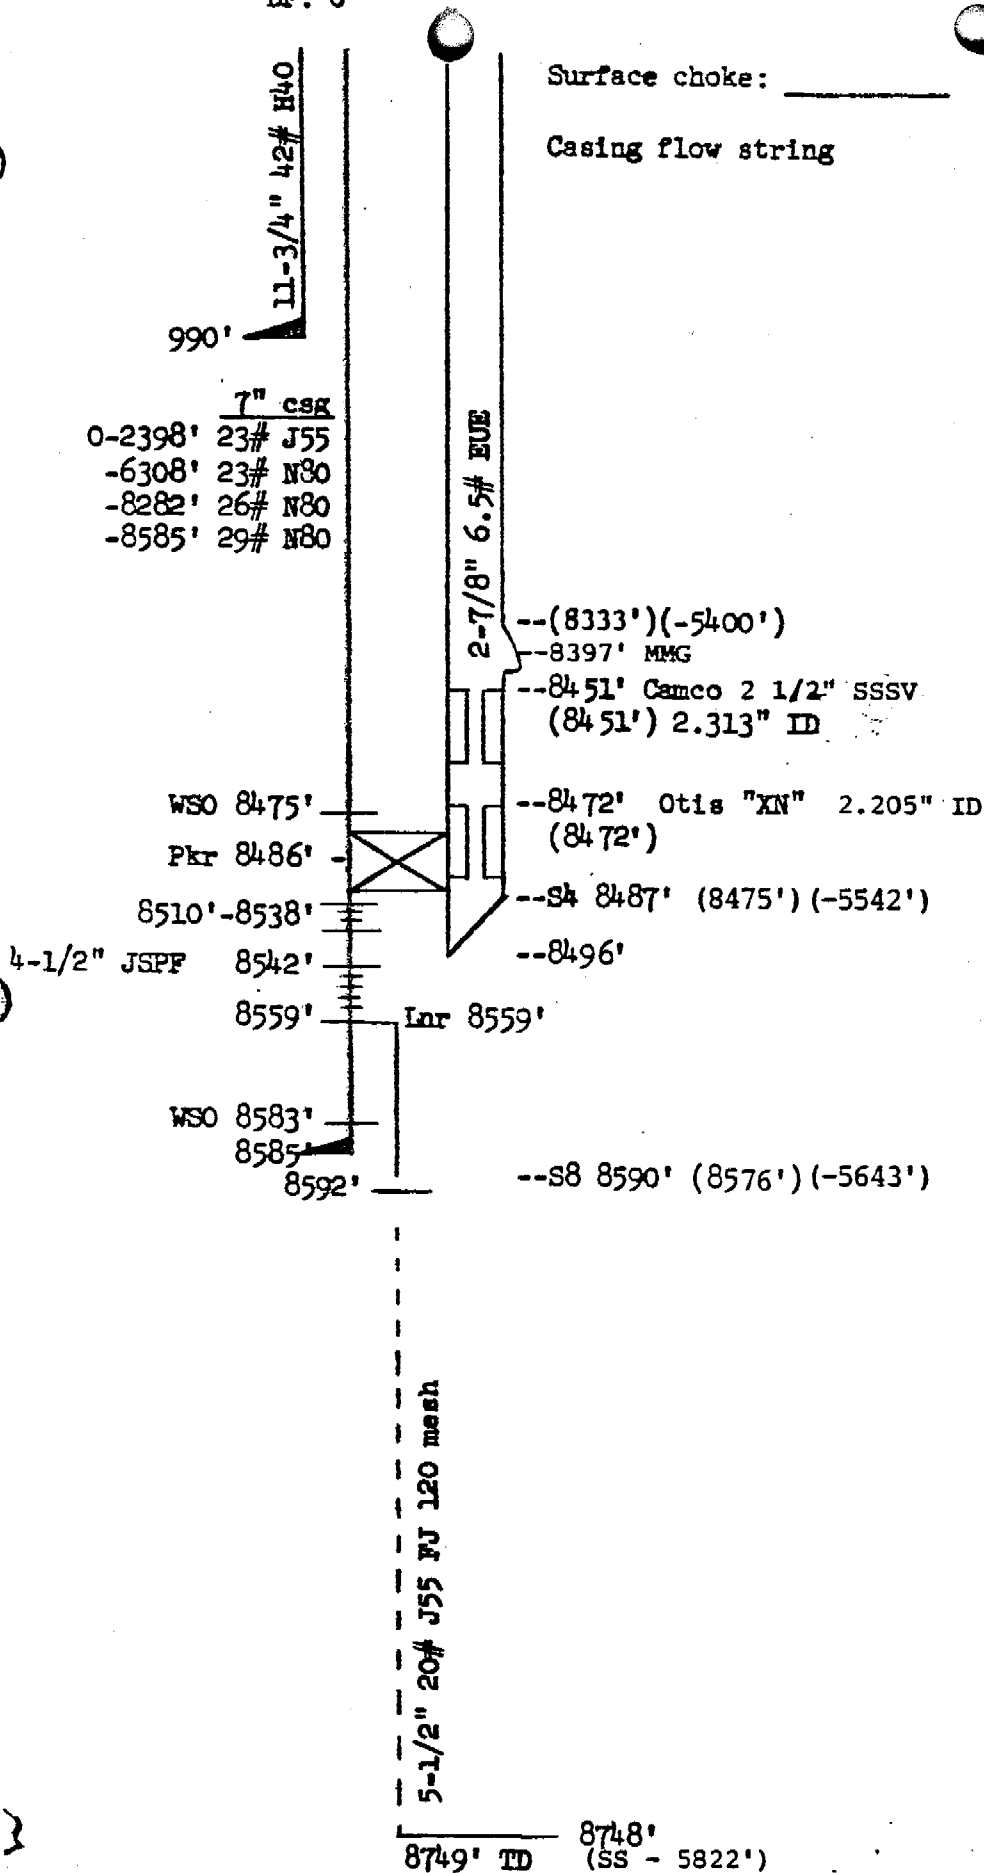

10/1/53 - Well spud  
 2/25/54 - Well completed  
 893' of 4-1/2" drill pipe + Johnston tester side tracked - old TD 4948' plugged back 3860'  
 5/24/73 - 6/6/73 Cleaned out to 8748', pressure tested csg, perforated for conversion to gas storage, ran tbg with gas lift valves  
 6/25/76 - 7/9/76 Cleaned out to 8748', ran tbg with SSSV  
 2/16/79-2/20/79 Replaced safety system

NOTE: Unable to use lower nipple - use M-lock for SSSV nipple. See wire-line tickets.

|          | WELL VOLUME |      |
|----------|-------------|------|
|          | Cu.Ft.      | Bbl. |
| Tubing   | 276         | 49   |
| Csg/Lnr. | 37          | 7    |
| Annulus  | 1469        | 262  |
