


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
1	UPDATED as of November 1, 2020														
2	SCE - Local RCI Solicitation	651 days	Tue 8/21/18	Tue 2/16/21											
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18											
4	SCE - RFA Release	0 days	Fri 11/9/18	Fri 11/9/18											
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18											
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19											
7	SCE - RFA Review with EE PRG	0 days	Tue 4/16/19	Tue 4/16/19											
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/21/19	Tue 5/21/19											
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20											
10	SCE - RFP Release	0 days	Wed 1/22/20	Wed 1/22/20											
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20											
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20											
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/7/20	Thu 5/7/20											
14	SCE - RFP Review with EE PRG	0 days	Tue 4/21/20	Tue 4/21/20											
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20											
16	SCE - Contract Review with EE PRG	0 days	Tue 8/18/20	Tue 8/18/20											
17	SCE - Final Award and Contract Signed	0 days	Wed 9/30/20	Wed 9/30/20											
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20											
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20											
20	SCE - Implementation Plan	32 days	Mon 1/4/21	Tue 2/16/21											
21	SCE - SW Lighting	510 days	Wed 4/3/19	Tue 3/16/21											
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19											
23	SCE - RFA Release	0 days	Tue 7/2/19	Tue 7/2/19											
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19											
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19											
26	SCE - RFA Review with EE PRG	0 days	Tue 9/17/19	Tue 9/17/19											
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/24/19	Tue 9/24/19											
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20											
29	SCE - RFP Release	0 days	Thu 2/6/20	Thu 2/6/20											
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20											
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20											
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/7/20	Thu 5/7/20											
33	SCE - RFP Review with EE PRG	0 days	Tue 4/21/20	Tue 4/21/20											
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20											
35	SCE - Contract Review with EE PRG	0 days	Tue 8/18/20	Tue 8/18/20											
36	SCE - Final Award and Contract Signed	0 days	Wed 9/30/20	Wed 9/30/20											
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20											
38	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20											

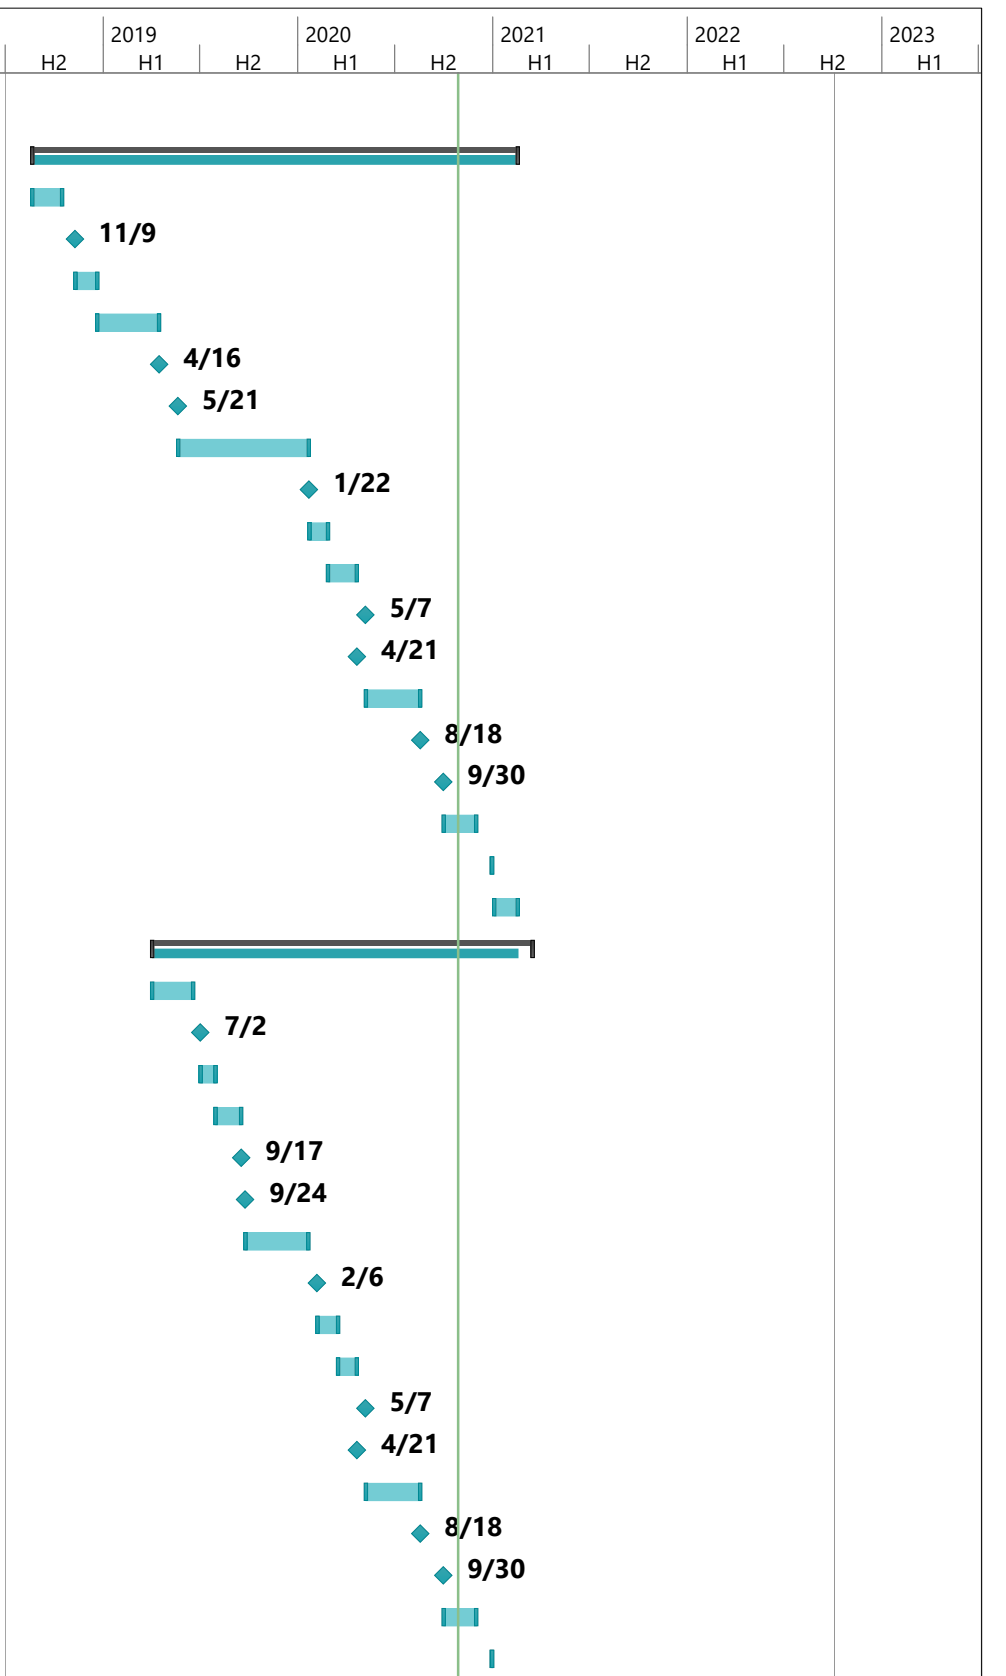

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
39	SCE - Implementation Plan	32 days	Mon 1/4/21	Tue 2/16/21											
40	SCE - Local PAG Solicitation - Local Public Sector	447 days	Mon 8/31/20	Tue 5/17/22											
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20											
42	SCE - RFA Release	0 days	Thu 11/5/20	Thu 11/5/20											
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20											
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21											
45	SCE - RFA Review with EE PRG	0 days	Tue 1/19/21	Tue 1/19/21											
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21											
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21											
48	SCE - RFP Release	0 days	Thu 4/1/21	Thu 4/1/21											
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21											
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21											
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/28/21	Mon 6/28/21											
52	SCE - RFP Review with EE PRG	0 days	Tue 6/15/21	Tue 6/15/21											
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21											
54	SCE - Contract Review with EE PRG	0 days	Tue 11/16/21	Tue 11/16/21											
55	SCE - Final Award and Contract Signed	0 days	Wed 12/15/21	Wed 12/15/21											
56	SCE - Submit Advice Letter	42 days	Thu 12/16/21	Fri 2/11/22											
57	SCE - Advice Letter Approved	1 day	Mon 3/21/22	Mon 3/21/22											
58	SCE - Implementation Plan	41 days	Tue 3/22/22	Tue 5/17/22											
59	SCE - Local PAG Solicitation - Local Agriculture	447 days	Mon 8/31/20	Tue 5/17/22											
60	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20											
61	SCE - RFA Release	0 days	Thu 11/5/20	Thu 11/5/20											
62	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20											
63	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21											
64	SCE - RFA Review with EE PRG	0 days	Tue 1/19/21	Tue 1/19/21											
65	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21											
66	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21											
67	SCE - RFP Release	0 days	Thu 4/1/21	Thu 4/1/21											
68	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21											
69	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21											
70	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/28/21	Mon 6/28/21											
71	SCE - RFP Review with EE PRG	0 days	Tue 6/15/21	Tue 6/15/21											
72	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21											
73	SCE - Contract Review with EE PRG	0 days	Tue 11/16/21	Tue 11/16/21											
74	SCE - Final Award and Contract Signed	0 days	Wed 12/15/21	Wed 12/15/21											
75	SCE - Submit Advice Letter	42 days	Thu 12/16/21	Fri 2/11/22											
76	SCE - Advice Letter Approved	1 day	Mon 3/21/22	Mon 3/21/22											

Project: IOU Master Task Timeli Date: Wed 10/28/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1		
77	SCE - Implementation Plan	41 days	Tue 3/22/22	Tue 5/17/22											
78	SCE - SW Water/Wastewater Solicitation	457 days	Mon 11/16/20	Tue 8/16/22											
79	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21											
80	SCE - RFA Release	0 days	Thu 3/4/21	Thu 3/4/21											
81	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21											
82	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21											
83	SCE - RFA Review with EE PRG	0 days	Tue 5/18/21	Tue 5/18/21											
84	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 5/27/21	Thu 5/27/21											
85	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21											
86	SCE - RFP Release	0 days	Thu 7/1/21	Thu 7/1/21											
87	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21											
88	SCE - RFP Evaluation	28 days	Fri 8/6/21	Tue 9/14/21											
89	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 9/27/21	Mon 9/27/21											
90	SCE - RFP Review with EE PRG	0 days	Tue 9/21/21	Tue 9/21/21											
91	SCE - Contract Negotiation and Development	96 days	Wed 9/22/21	Wed 2/2/22											
92	SCE - Contract Review with EE PRG	0 days	Tue 2/15/22	Tue 2/15/22											
93	SCE - Final Award and Contract Signed	0 days	Thu 3/31/22	Thu 3/31/22											
94	SCE - Submit Advice Letter	24 days	Fri 4/1/22	Wed 5/4/22											
95	SCE - Advice Letter Approved	1 day	Fri 6/3/22	Fri 6/3/22											
96	SCE - Implementation Plan	33 days	Fri 7/1/22	Tue 8/16/22											
97	SCE - SW ETP Solicitation	423 days	Fri 5/1/20	Tue 12/14/21											
98	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20											
99	SCE - RFA Release	0 days	Tue 8/4/20	Tue 8/4/20											
100	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20											
101	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20											
102	SCE - RFA Review with EE PRG	0 days	Tue 10/20/20	Tue 10/20/20											
103	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/27/20	Tue 10/27/20											
104	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20											
105	SCE - RFP Release	0 days	Tue 12/8/20	Tue 12/8/20											
106	SCE - RFP Proposal Creation Duration	34 days	Tue 12/8/20	Fri 1/22/21											
107	SCE - RFP Evaluation	28 days	Mon 1/25/21	Wed 3/3/21											
108	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 3/23/21	Tue 3/23/21											
109	SCE - RFP Review with EE PRG	0 days	Tue 3/16/21	Tue 3/16/21											
110	SCE - Contract Negotiation and Development	61 days	Wed 3/17/21	Wed 6/9/21											
111	SCE - Contract Review with EE PRG	0 days	Tue 6/15/21	Tue 6/15/21											
112	SCE - Final Award and Contract Signed	0 days	Fri 8/6/21	Fri 8/6/21											
113	SCE - Submit Advice Letter	25 days	Mon 8/9/21	Fri 9/10/21											
114	SCE - Advice Letter Approved	1 day	Fri 10/15/21	Fri 10/15/21											


Project: IOU Master Task Timeli Date: Wed 10/28/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
115	SCE - Implementation Plan	42 days	Mon 10/18/21	Tue 12/14/21											
116	SCE - SW Higher-Education Solicitation	449 days?	Thu 10/1/20	Tue 6/21/22											
117	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21											
118	SCE - RFA Release	0 days	Thu 2/4/21	Thu 2/4/21											
119	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21											
120	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21											
121	SCE - RFA Review with EE PRG	0 days	Tue 4/20/21	Tue 4/20/21											
122	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 4/29/21	Thu 4/29/21											
123	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21											
124	SCE - RFP Release	0 days	Fri 5/28/21	Fri 5/28/21											
125	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21											
126	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21											
127	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/30/21	Mon 8/30/21											
128	SCE - RFP Review with EE PRG	0 days	Tue 8/17/21	Tue 8/17/21											
129	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22											
130	SCE - Contract Review with EE PRG	0 days	Tue 1/18/22	Tue 1/18/22											
131	SCE - Final Award and Contract Signed	0 days	Wed 2/9/22	Wed 2/9/22											
132	SCE - Submit Advice Letter	23 days	Thu 2/10/22	Mon 3/14/22											
133	SCE - Advice Letter Approved	1 day	Fri 4/15/22	Fri 4/15/22											
134	SCE - Implementation Plan	47 days	Mon 4/18/22	Tue 6/21/22											
135															
136															
137															
138	SCG - Local Single Family Solicitation	710 days	Sun 7/1/18	Fri 3/19/21											
139	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18											
140	SCG - RFA Release	0 days	Mon 11/26/18	Mon 11/26/18											
141	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19											
142	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19											
143	SCG - RFA Review with EE PRG	0 days	Tue 3/5/19	Tue 3/5/19											
144	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/3/19	Mon 6/3/19											
145	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19											
146	SCG - RFP Release	0 days	Wed 7/31/19	Wed 7/31/19											
147	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19											
148	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19											
149	SCG - RFP Review with EE PRG	0 days	Tue 11/5/19	Tue 11/5/19											
150	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
151	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20											
152	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
153	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20											
154	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20											
155	SCG - Advice Letter Approved	1 day	Fri 1/15/21	Fri 1/15/21											
156	SCG - Implementation Plan	45 days	Mon 1/18/21	Fri 3/19/21											
157	SCG - Local Multi-family Solicitation	730 days	Sun 7/1/18	Fri 4/16/21											
158	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18											
159	SCG - RFA Release	0 days	Mon 11/26/18	Mon 11/26/18											
160	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19											
161	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19											
162	SCG - RFA Review with EE PRG	0 days	Tue 4/2/19	Tue 4/2/19											
163	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/3/19	Mon 6/3/19											
164	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19											
165	SCG - RFP Release	0 days	Wed 7/31/19	Wed 7/31/19											
166	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19											
167	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19											
168	SCG - RFP Review with EE PRG	0 days	Tue 11/5/19	Tue 11/5/19											
169	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
170	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20											
171	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20											
172	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20											
173	SCG - Submit Advice Letter	32 days	Thu 10/1/20	Fri 11/13/20											
174	SCG - Advice Letter Approved	1 day	Fri 2/12/21	Fri 2/12/21											
175	SCG - Implementation Plan	45 days	Mon 2/15/21	Fri 4/16/21											
176	SCG - Local Small/Medium Commercial Solicitation	679 days	Tue 9/4/18	Fri 4/9/21											
177	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19											
178	SCG - RFA Release	0 days	Thu 1/31/19	Thu 1/31/19											
179	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19											
180	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19											
181	SCG - RFA Review with EE PRG	0 days	Tue 6/4/19	Tue 6/4/19											
182	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 8/1/19	Thu 8/1/19											
183	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19											
184	SCG - RFP Release	0 days	Fri 8/23/19	Fri 8/23/19											
185	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19											
186	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19											
187	SCG - RFP Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
188	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
189	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20											
190	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20											

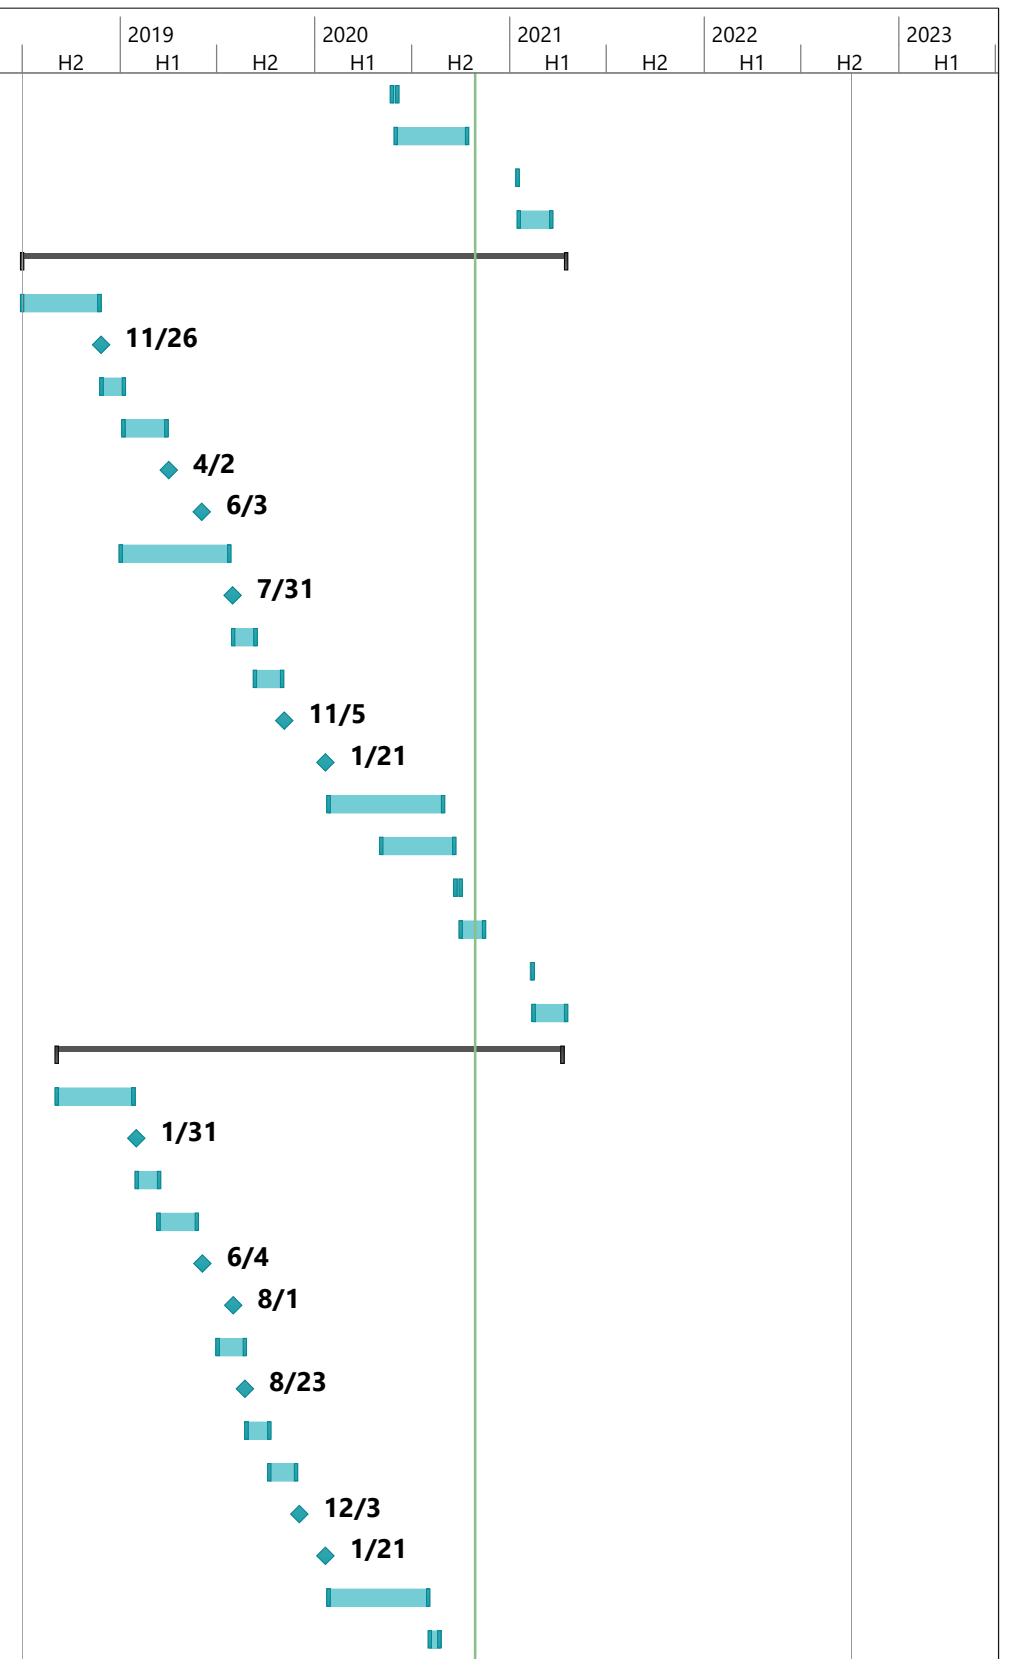

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
191	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20											
192	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20											
193	SCG - Advice Letter Approved	1 day	Fri 2/5/21	Fri 2/5/21											
194	SCG - Implementation Plan	45 days	Mon 2/8/21	Fri 4/9/21											
195	SCG - Local Small/Medium Public Solicitation	674 days	Tue 9/4/18	Fri 4/2/21											
196	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19											
197	SCG - RFA Release	0 days	Thu 1/31/19	Thu 1/31/19											
198	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19											
199	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19											
200	SCG - RFA Review with EE PRG	0 days	Tue 6/4/19	Tue 6/4/19											
201	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 8/1/19	Thu 8/1/19											
202	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19											
203	SCG - RFP Release	0 days	Fri 8/23/19	Fri 8/23/19											
204	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19											
205	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19											
206	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19											
207	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
208	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20											
209	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20											
210	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20											
211	SCG - Submit Advice Letter	44 days	Tue 9/1/20	Fri 10/30/20											
212	SCG - Advice Letter Approved	0 days	Mon 2/1/21	Mon 2/1/21											
213	SCG - Implementation Plan	44 days	Tue 2/2/21	Fri 4/2/21											
214	SCG - Statewide POS Food Service Solicitation	595 days	Mon 1/21/19	Fri 4/30/21											
215	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19											
216	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19											
217	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19											
218	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19											
219	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
220	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20											
221	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19											
222	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20											
223	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20											
224	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20											
225	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
226	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
227	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20											
228	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20											

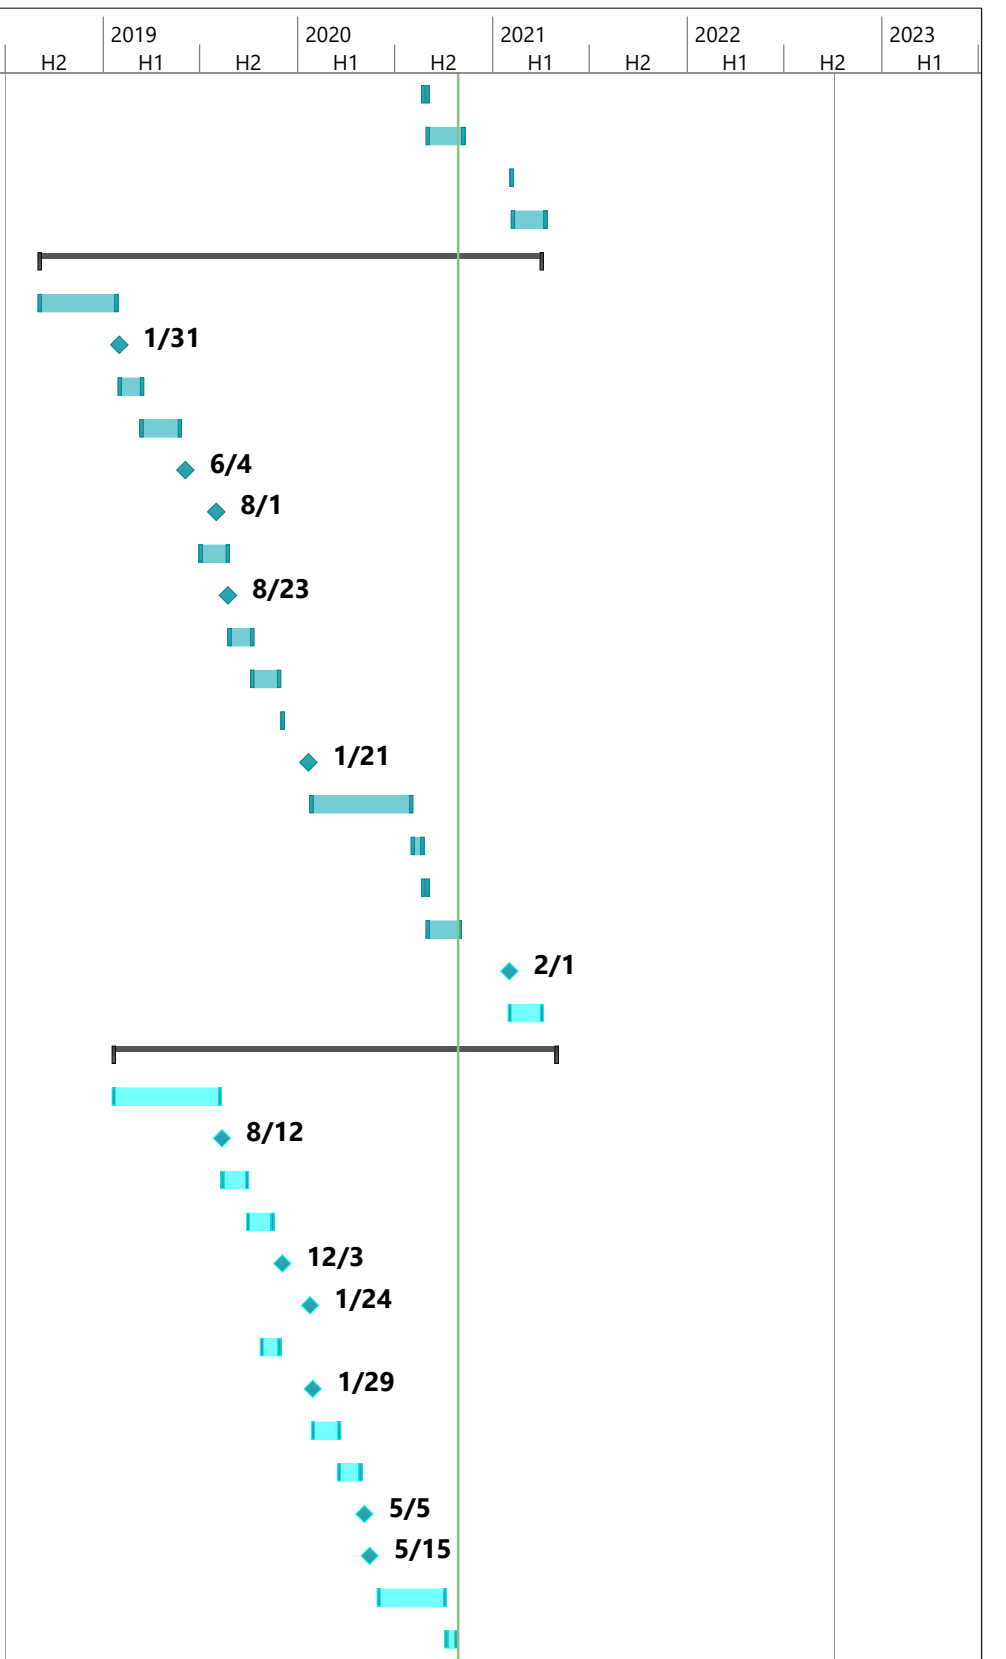

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
229	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20											
230	SCG - Submit Advice Letter	21 days	Mon 11/2/20	Mon 11/30/20											
231	SCG - Advice Letter Approved	0 days	Fri 2/26/21	Fri 2/26/21											
232	SCG - Implementation Plan	45 days	Mon 3/1/21	Fri 4/30/21											
233	SCG - Statewide Midstream Water Heating Solicitation	595 days	Mon 1/21/19	Fri 4/30/21											
234	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19											
235	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19											
236	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19											
237	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19											
238	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19											
239	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20											
240	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19											
241	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20											
242	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20											
243	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20											
244	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
245	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
246	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20											
247	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20											
248	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20											
249	SCG - Submit Advice Letter	21 days	Mon 11/2/20	Mon 11/30/20											
250	SCG - Advice Letter Approved	0 days	Fri 2/26/21	Fri 2/26/21											
251	SCG - Implementation Plan	45 days	Mon 3/1/21	Fri 4/30/21											
252	SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Sat 10/30/21											
253	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20											
254	SCG - RFA Release	0 days	Wed 2/12/20	Wed 2/12/20											
255	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20											
256	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20											
257	SCG - RFA Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20											
258	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20											
259	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20											
260	SCG - RFP Release	0 days	Fri 8/21/20	Fri 8/21/20											
261	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20											
262	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20											
263	SCG - RFP Review with EE PRG	0 days	Tue 12/1/20	Tue 12/1/20											
264	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/8/20	Tue 12/8/20											
265	SCG - Contract Negotiation and Development	75 days	Mon 12/21/20	Fri 4/2/21											
266	SCG - Contract Review with EE PRG	14 days	Tue 4/6/21	Fri 4/23/21											

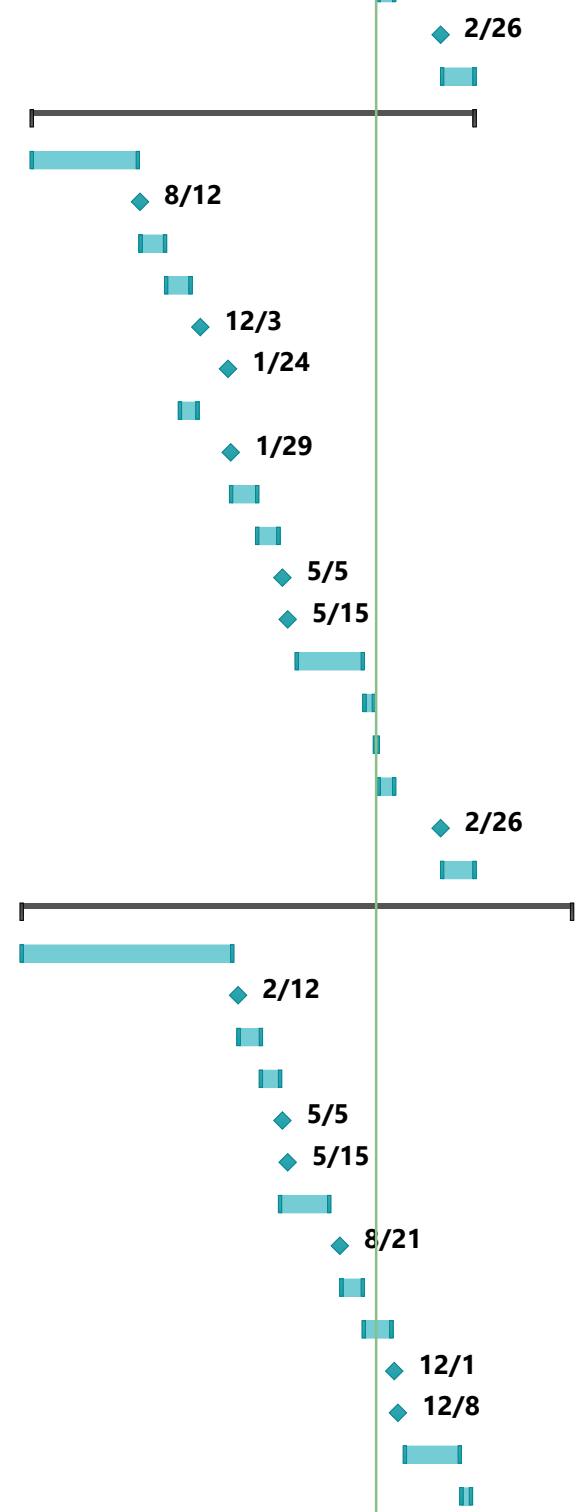

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
267	SCG - Final Award and Contract Signed	5 days	Mon 4/26/21	Fri 4/30/21											
268	SCG - Submit Advice Letter	22 days	Sat 5/1/21	Sun 5/30/21											
269	SCG - Advice Letter Approved	0 days	Tue 8/31/21	Tue 8/31/21											
270	SCG - Implementation Plan	44 days	Wed 9/1/21	Sat 10/30/21											
271	SCG - Local Manufactured Housing Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
272	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
273	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
274	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
275	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
276	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
277	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
278	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
279	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20											
280	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
281	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
282	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20											
283	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20											
284	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
285	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											
286	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
287	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											
288	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
289	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
290	SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
291	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
292	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
293	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
294	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
295	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
296	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
297	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
298	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20											
299	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
300	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
301	SCG - RFP Review with EE PRG	0 days	Tue 10/6/20	Tue 10/6/20											
302	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/13/20	Tue 10/13/20											
303	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
304	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
305	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
306	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											
307	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
308	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
309	SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21											
310	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20											
311	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20											
312	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20											
313	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20											
314	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20											
315	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20											
316	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20											
317	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20											
318	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20											
319	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20											
320	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20											
321	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20											
322	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20											
323	SCG - Contract Review with EE PRG	14 days	Tue 12/1/20	Fri 12/18/20											
324	SCG - Final Award and Contract Signed	9 days	Mon 12/21/20	Thu 12/31/20											
325	SCG - Submit Advice Letter	21 days	Fri 1/1/21	Fri 1/29/21											
326	SCG - Advice Letter Approved	0 days	Fri 4/30/21	Fri 4/30/21											
327	SCG - Implementation Plan	43 days	Mon 5/3/21	Wed 6/30/21											
328	SCG - Local Behavioral Solicitation	413 days	Fri 5/1/20	Tue 11/30/21											
329	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20											
330	SCG - RFA Release	0 days	Fri 8/21/20	Fri 8/21/20											
331	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20											
332	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20											
333	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20											
334	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 11/10/20	Tue 11/10/20											
335	SCG - RFP Preparation	40 days	Thu 10/1/20	Wed 11/25/20											
336	SCG - RFP Release	0 days	Fri 12/11/20	Fri 12/11/20											
337	SCG - RFP Proposal Creation Duration	30 days	Mon 12/14/20	Fri 1/22/21											
338	SCG - RFP Evaluation	25 days	Mon 1/25/21	Fri 2/26/21											
339	SCG - RFP Review with EE PRG	0 days	Tue 3/2/21	Tue 3/2/21											
340	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 3/9/21	Tue 3/9/21											
341	SCG - Contract Negotiation and Development	30 days	Mon 3/22/21	Fri 4/30/21											
342	SCG - Contract Review with EE PRG	14 days	Tue 5/4/21	Fri 5/21/21											

Project: IOU Master Task Timeli Date: Wed 10/28/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
343	SCG - Final Award and Contract Signed	6 days	Mon 5/24/21	Mon 5/31/21											
344	SCG - Submit Advice Letter	22 days	Tue 6/1/21	Wed 6/30/21											
345	SCG - Advice Letter Approved	0 days	Thu 9/30/21	Thu 9/30/21											
346	SCG - Implementation Plan	43 days	Fri 10/1/21	Tue 11/30/21											
347	SCG - Outreach Solicitation	434 days	Sun 11/1/20	Thu 6/30/22											
348	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
349	SCG - RFA Release	0 days	Fri 2/19/21	Fri 2/19/21											
350	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
351	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
352	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
353	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
354	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
355	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
356	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
357	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
358	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
359	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
360	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
361	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											
362	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
363	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											
364	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
365	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
366	SCG - Marketplace Solicitation	435 days?	Sun 11/1/20	Thu 6/30/22											
367	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
368	SCG - RFA Release	1 day	Fri 2/19/21	Fri 2/19/21											
369	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
370	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
371	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
372	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
373	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
374	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
375	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
376	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
377	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
378	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
379	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
380	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
381	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
382	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											
383	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
384	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
385	SCG - Public Sector Segment Solicitation	434 days	Sun 11/1/20	Thu 6/30/22											
386	SCG - RFA Preparation	65 days	Sun 11/1/20	Thu 1/28/21											
387	SCG - RFA Release	0 days	Fri 2/19/21	Fri 2/19/21											
388	SCG - RFA Abstract Creation Duration	25 days	Mon 2/22/21	Fri 3/26/21											
389	SCG - RFA Evaluation	25 days	Mon 3/29/21	Fri 4/30/21											
390	SCG - RFA Review with EE PRG	0 days	Tue 5/4/21	Tue 5/4/21											
391	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 5/11/21	Tue 5/11/21											
392	SCG - RFP Preparation	42 days	Thu 4/1/21	Fri 5/28/21											
393	SCG - RFP Release	0 days	Fri 6/11/21	Fri 6/11/21											
394	SCG - RFP Proposal Creation Duration	30 days	Mon 6/14/21	Fri 7/23/21											
395	SCG - RFP Evaluation	30 days	Mon 7/26/21	Fri 9/3/21											
396	SCG - RFP Review with EE PRG	0 days	Tue 9/7/21	Tue 9/7/21											
397	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 9/14/21	Tue 9/14/21											
398	SCG - Contract Negotiation and Development	35 days	Mon 10/18/21	Fri 12/3/21											
399	SCG - Contract Review with EE PRG	9 days	Tue 12/7/21	Fri 12/17/21											
400	SCG - Final Award and Contract Signed	10 days	Mon 12/20/21	Fri 12/31/21											
401	SCG - Submit Advice Letter	21 days	Mon 1/3/22	Mon 1/31/22											
402	SCG - Advice Letter Approved	0 days	Fri 4/29/22	Fri 4/29/22											
403	SCG - Implementation Plan	44 days	Mon 5/2/22	Thu 6/30/22											
404	SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Sun 7/31/22											
405	SCG - RFA Preparation	63 days	Tue 12/1/20	Thu 2/25/21											
406	SCG - RFA Release	0 days	Fri 3/19/21	Fri 3/19/21											
407	SCG - RFA Abstract Creation Duration	25 days	Mon 3/22/21	Fri 4/23/21											
408	SCG - RFA Evaluation	25 days	Mon 4/26/21	Fri 5/28/21											
409	SCG - RFA Review with EE PRG	0 days	Tue 6/1/21	Tue 6/1/21											
410	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/8/21	Tue 6/8/21											
411	SCG - RFP Preparation	46 days	Sat 5/1/21	Fri 7/2/21											
412	SCG - RFP Release	0 days	Fri 7/16/21	Fri 7/16/21											
413	SCG - RFP Proposal Creation Duration	30 days	Mon 7/19/21	Fri 8/27/21											
414	SCG - RFP Evaluation	25 days	Mon 8/30/21	Fri 10/1/21											
415	SCG - RFP Review with EE PRG	0 days	Tue 10/5/21	Tue 10/5/21											
416	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 10/12/21	Tue 10/12/21											
417	SCG - Contract Negotiation and Development	46 days	Fri 10/29/21	Fri 12/31/21											
418	SCG - Contract Review with EE PRG	14 days	Tue 1/4/22	Fri 1/21/22											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
419	SCG - Final Award and Contract Signed	6 days	Mon 1/24/22	Mon 1/31/22											
420	SCG - Submit Advice Letter	20 days	Tue 2/1/22	Mon 2/28/22											
421	SCG - Advice Letter Approved	0 days	Tue 5/31/22	Tue 5/31/22											
422	SCG - Implementation Plan	44 days	Wed 6/1/22	Sun 7/31/22											
423															
424	SDG&E - Small Commercial (<20kW)	612 days	Wed 8/1/18	Thu 12/3/20											
425	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18											
426	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18											
427	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18											
428	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19											
429	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19											
430	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19											
431	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19											
432	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19											
433	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19											
434	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19											
435	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20											
436	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20											
437	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20											
438	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20											
439	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20											
440	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
441	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
442	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20											
443	SDG&E - Large Commercial (>20kW)	612 days	Wed 8/1/18	Thu 12/3/20											
444	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18											
445	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18											
446	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18											
447	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19											
448	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19											
449	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19											
450	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19											
451	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19											
452	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19											
453	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19											
454	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20											
455	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20											
456	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20											



Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
457	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20											
458	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20											
459	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
460	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
461	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20											
462	SDG&E - Residential Multi-Family	586 days	Thu 9/6/18	Thu 12/3/20											
463	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18											
464	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19											
465	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18											
466	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19											
467	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18											
468	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19											
469	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19											
470	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19											
471	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19											
472	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19											
473	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19											
474	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
475	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20											
476	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20											
477	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20											
478	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20											
479	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20											
480	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20											
481	SDG&E - SW HVAC	586 days	Thu 11/1/18	Fri 1/29/21											
482	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19											
483	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19											
484	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19											
485	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19											
486	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19											
487	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19											
488	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19											
489	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19											
490	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19											
491	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19											
492	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20											
493	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
494	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20											

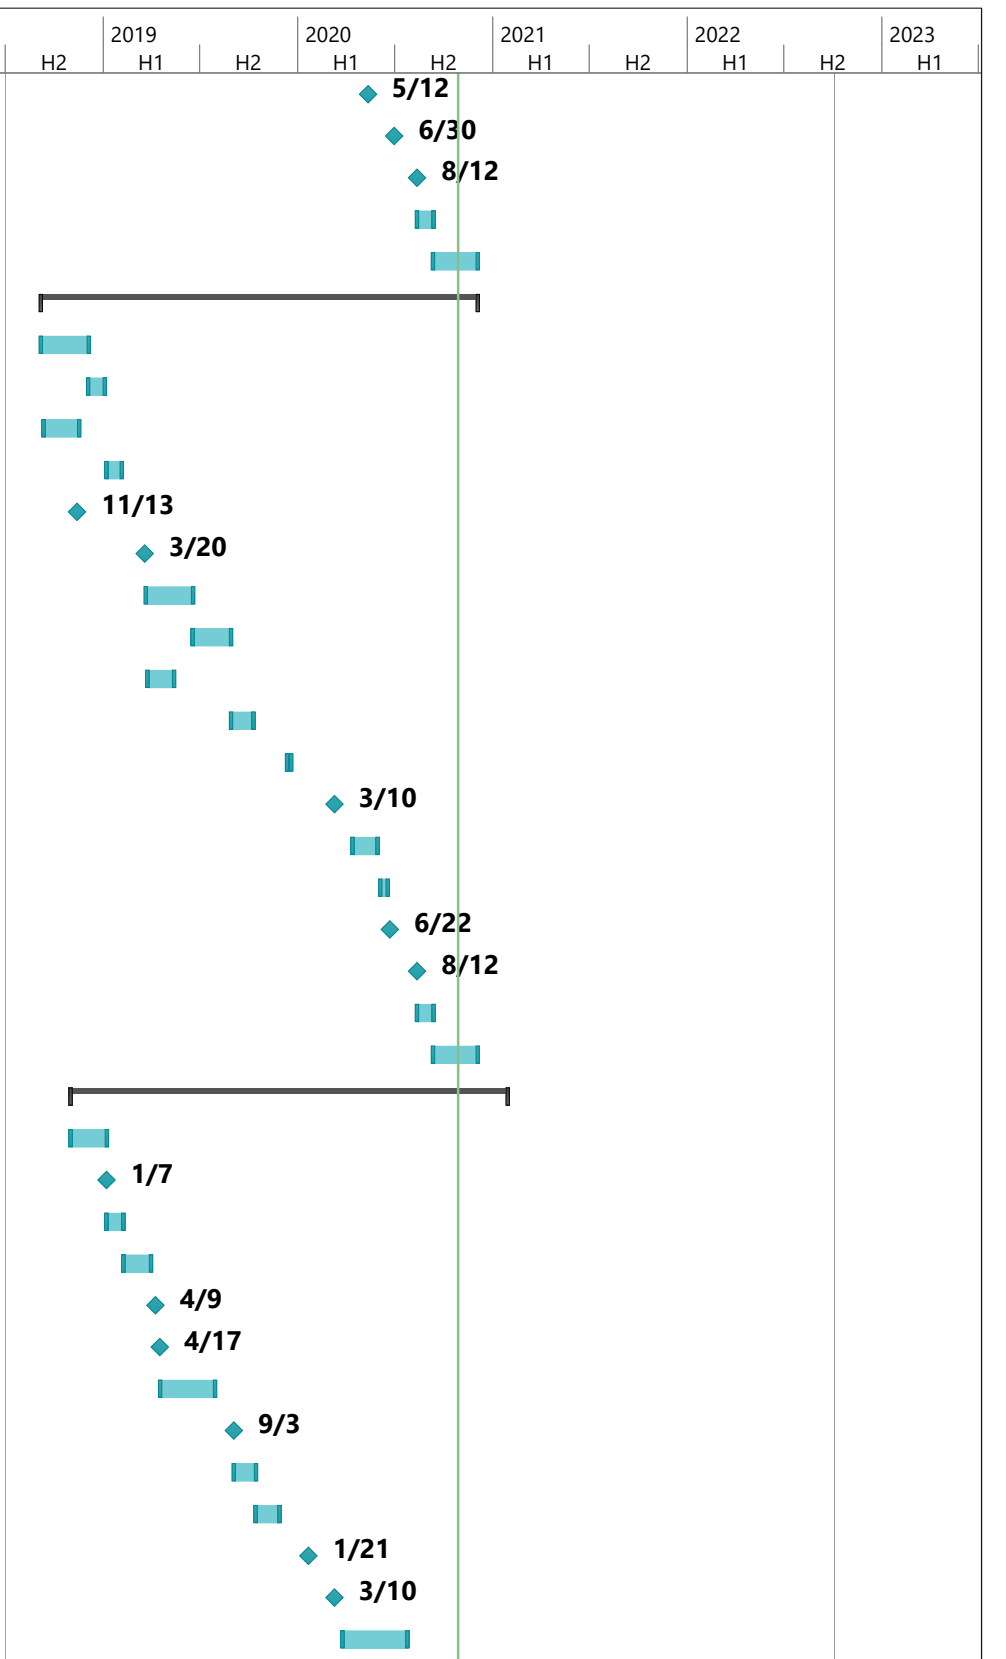

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
495	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20											
496	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20											
497	SDG&E - Submit Advice Letter	0 days	Thu 11/19/20	Thu 11/19/20											
498	SDG&E - Advice Letter Approved														
499	SDG&E - Implementation Plan	0 days	Fri 1/29/21	Fri 1/29/21											
500	SDG&E - SW PLA	633 days?	Mon 1/28/19	Wed 6/30/21											
501	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19											
502	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19											
503	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19											
504	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19											
505	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19											
506	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19											
507	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19											
508	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20											
509	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20											
510	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20											
511	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20											
512	SDG&E - Selection Review with EE PRG	0 days	Tue 10/13/20	Tue 10/13/20											
513	SDG&E - Contract Negotiation and Development	51 days	Mon 11/16/20	Mon 1/25/21											
514	SDG&E - Contract Review with EE PRG	0 days	Tue 2/9/21	Tue 2/9/21											
515	SDG&E - Final Award and Contract Signed	0 days	Fri 2/26/21	Fri 2/26/21											
516	SDG&E - Submit Advice Letter	0 days	Tue 3/30/21	Tue 3/30/21											
517	SDG&E - Advice Letter Approved														
518	SDG&E - Implementation Plan	0 days	Wed 6/30/21	Wed 6/30/21											
519	SDG&E - Residential Single Family	501 days?	Mon 7/1/19	Tue 6/1/21											
520	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19											
521	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19											
522	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19											
523	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20											
524	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19											
525	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20											
526	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20											
527	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20											
528	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20											
529	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20											
530	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20											
531	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20											
532	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20											

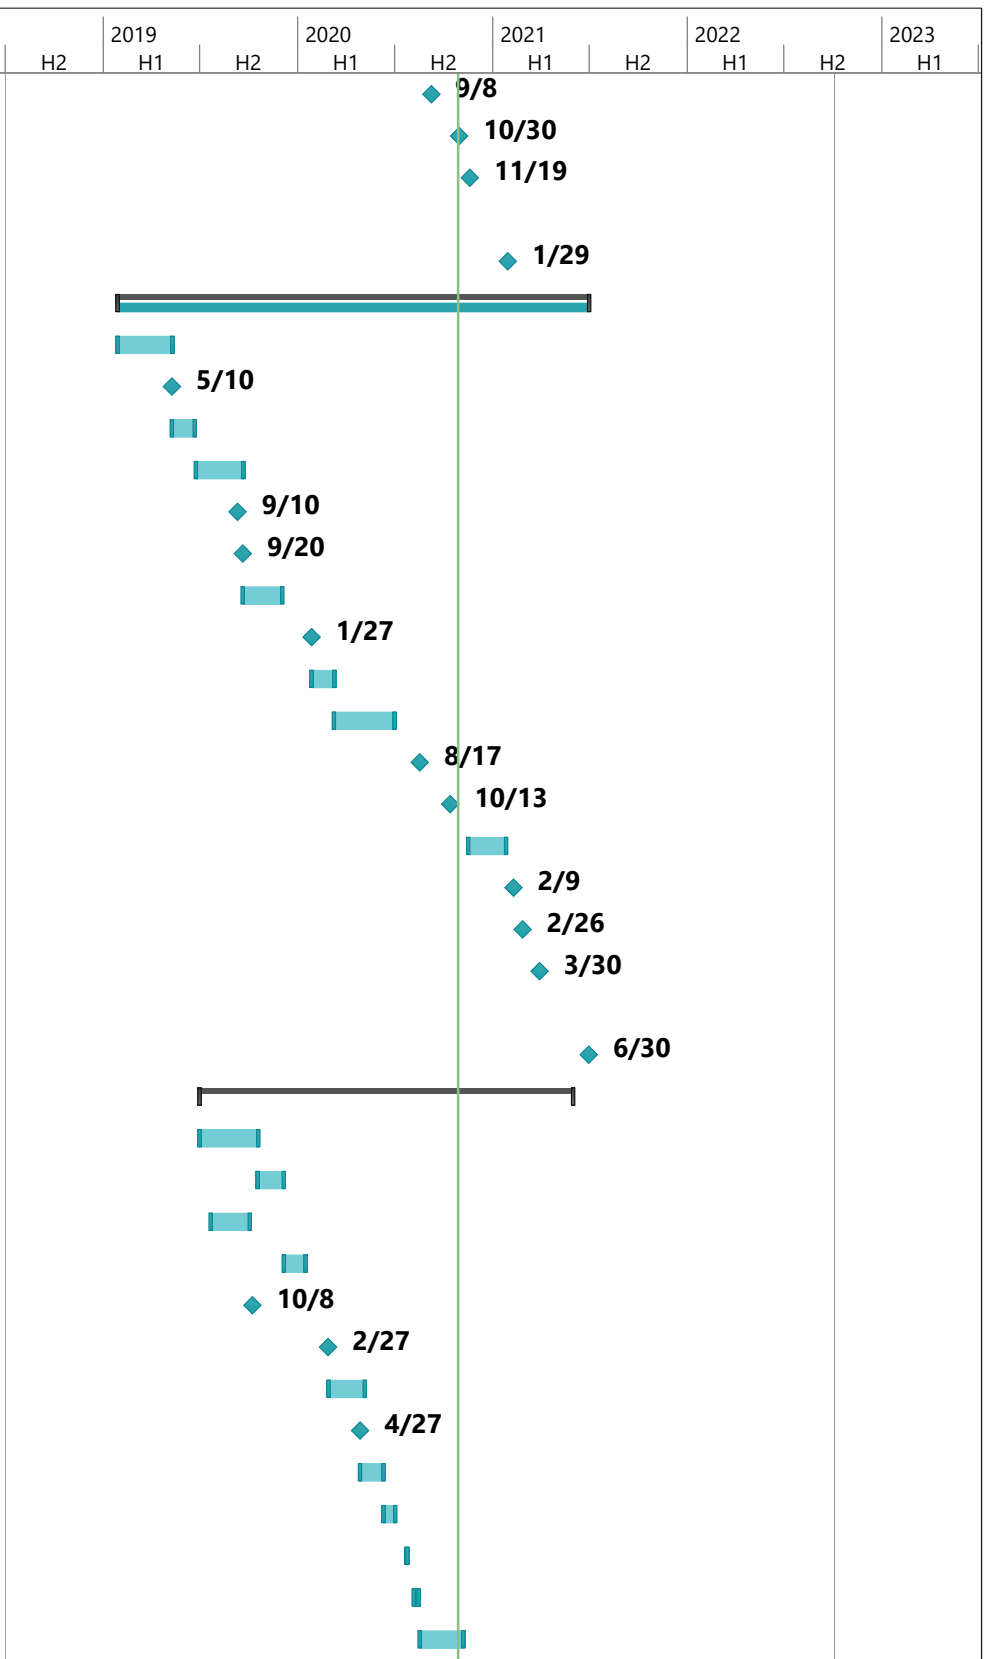

Project: IOU Master Task Timeli Date: Wed 10/28/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
533	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20											
534	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21											
535	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21											
536	SDG&E - Advice Letter Approved														
537	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21											
538	SDG&E - Federal	496 days?	Mon 7/1/19	Tue 5/25/21											
539	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19											
540	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19											
541	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19											
542	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20											
543	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
544	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20											
545	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20											
546	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20											
547	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20											
548	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20											
549	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20											
550	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20											
551	SDG&E - Contract Negotiation and Development	45 days	Thu 11/19/20	Wed 1/20/21											
552	SDG&E - Contract Review with EE PRG	0 days	Tue 1/12/21	Tue 1/12/21											
553	SDG&E - Final Award and Contract Signed	0 days	Mon 1/25/21	Mon 1/25/21											
554	SDG&E - Submit Advice Letter	0 days	Thu 2/25/21	Thu 2/25/21											
555	SDG&E - Advice Letter Approved														
556	SDG&E - Implementation Plan	0 days	Tue 5/25/21	Tue 5/25/21											
557	SDG&E - K-12	496 days?	Mon 7/1/19	Tue 5/25/21											
558	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19											
559	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19											
560	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19											
561	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20											
562	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20											
563	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20											
564	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20											
565	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20											
566	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20											
567	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20											
568	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20											
569	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20											
570	SDG&E - Contract Negotiation and Development	45 days	Thu 11/19/20	Wed 1/20/21											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
571	SDG&E - Contract Review with EE PRG	0 days	Tue 1/12/21	Tue 1/12/21											
572	SDG&E - Final Award and Contract Signed	0 days	Mon 1/25/21	Mon 1/25/21											
573	SDG&E - Submit Advice Letter	0 days	Thu 2/25/21	Thu 2/25/21											
574	SDG&E - Advice Letter Approved														
575	SDG&E - Implementation Plan	0 days	Tue 5/25/21	Tue 5/25/21											
576	SDG&E - Local Governments	304 days?	Tue 10/13/20	Fri 12/10/21											
577	SDG&E - RFA Preparation														
578	SDG&E - RFA Release														
579	SDG&E - RFA Abstract Creation Duration														
580	SDG&E - RFA Evaluation														
581	SDG&E - RFA Review with EE PRG														
582	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
583	SDG&E - RFP Preparation														
584	SDG&E - RFP Release														
585	SDG&E - RFP Proposal Creation Duration														
586	SDG&E - RFP Evaluation														
587	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
588	SDG&E - Selection Review with EE PRG														
589	SDG&E - Contract Negotiation and Development														
590	SDG&E - Contract Review with EE PRG														
591	SDG&E - Final Award and Contract Signed														
592	SDG&E - Submit Advice Letter														
593	SDG&E - Advice Letter Approved														
594	SDG&E - Implementation Plan														
595	*SDG&E - Agriculture Growers	304 days?	Mon 2/1/21	Thu 3/31/22											
596	SDG&E - RFA Preparation														
597	SDG&E - RFA Release														
598	SDG&E - RFA Abstract Creation Duration														
599	SDG&E - RFA Evaluation														
600	SDG&E - RFA Review with EE PRG														
601	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
602	SDG&E - RFP Preparation														
603	SDG&E - RFP Release														
604	SDG&E - RFP Proposal Creation Duration														
605	SDG&E - RFP Evaluation														
606	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
607	SDG&E - Selection Review with EE PRG														
608	SDG&E - Contract Negotiation and Development														

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H1	
609	SDG&E - Contract Review with EE PRG														
610	SDG&E - Final Award and Contract Signed														
611	SDG&E - Submit Advice Letter														
612	SDG&E - Advice Letter Approved														
613	SDG&E - Implementation Plan														
614	*SDG&E - Industrial/Port Tenants	304 days?	Mon 2/1/21	Thu 3/31/22											
615	SDG&E - RFA Preparation														
616	SDG&E - RFA Release														
617	SDG&E - RFA Abstract Creation Duration														
618	SDG&E - RFA Evaluation														
619	SDG&E - RFA Review with EE PRG														
620	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
621	SDG&E - RFP Preparation														
622	SDG&E - RFP Release														
623	SDG&E - RFP Proposal Creation Duration														
624	SDG&E - RFP Evaluation														
625	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
626	SDG&E - Selection Review with EE PRG														
627	SDG&E - Contract Negotiation and Development														
628	SDG&E - Contract Review with EE PRG														
629	SDG&E - Final Award and Contract Signed														
630	SDG&E - Submit Advice Letter														
631	SDG&E - Advice Letter Approved														
632	SDG&E - Implementation Plan														
633	*SDG&E - SW Downstream Res HVAC	326 days?	Mon 7/5/21	Mon 10/3/22											
634	SDG&E - RFA Preparation														
635	SDG&E - RFA Release														
636	SDG&E - RFA Abstract Creation Duration														
637	SDG&E - RFA Evaluation														
638	SDG&E - RFA Review with EE PRG														
639	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
640	SDG&E - RFP Preparation														
641	SDG&E - RFP Release														
642	SDG&E - RFP Proposal Creation Duration														
643	SDG&E - RFP Evaluation														
644	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
645	SDG&E - Selection Review with EE PRG														
646	SDG&E - Contract Negotiation and Development														

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
647	SDG&E - Contract Review with EE PRG														
648	SDG&E - Final Award and Contract Signed														
649	SDG&E - Submit Advice Letter														
650	SDG&E - Advice Letter Approved														
651	SDG&E - Implementation Plan														
652	*SDG&E - Local/Residential Behavioral	324 days?	Mon 4/5/21	Thu 6/30/22											
653	SDG&E - RFA Preparation														
654	SDG&E - RFA Release														
655	SDG&E - RFA Abstract Creation Duration														
656	SDG&E - RFA Evaluation														
657	SDG&E - RFA Review with EE PRG														
658	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder														
659	SDG&E - RFP Preparation														
660	SDG&E - RFP Release														
661	SDG&E - RFP Proposal Creation Duration														
662	SDG&E - RFP Evaluation														
663	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder														
664	SDG&E - Selection Review with EE PRG														
665	SDG&E - Contract Negotiation and Development														
666	SDG&E - Contract Review with EE PRG														
667	SDG&E - Final Award and Contract Signed														
668	SDG&E - Submit Advice Letter														
669	SDG&E - Advice Letter Approved														
670	SDG&E - Implementation Plan														
671	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change														
672															
673	Local Multi-Sector (25% outsource)	616 days?	Wed 8/1/18	Wed 12/9/20											
674	PG&E RFA Preparation	83 days	Wed 8/1/18	Fri 11/23/18											
675	PG&E RFA Release	1 day	Wed 11/28/18	Wed 11/28/18											
676	PG&E RFA Abstract Creation Duration	34 days	Wed 11/28/18	Mon 1/14/19											
677	PG&E RFA Evaluation	22 days	Fri 1/18/19	Mon 2/18/19											
678	PG&E RFA Review with EE PRG	3 days	Thu 2/21/19	Mon 2/25/19											
679	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/11/19	Fri 3/15/19											
680	PG&E RFP Preparation	75 days	Mon 2/25/19	Fri 6/7/19											
681	PG&E RFP Release	1 day	Wed 6/12/19	Wed 6/12/19											
682	PG&E RFP Proposal Creation Duration	37 days	Wed 6/12/19	Thu 8/1/19											
683	PG&E RFP Evaluation	120 days	Mon 8/5/19	Fri 1/17/20											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
684	PG&E RFP Review with EE PRG	4 days	Tue 1/28/20	Fri 1/31/20											
685	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	11 days	Mon 2/3/20	Mon 2/17/20											
686	PG&E Contract Negotiation and Development	70 days	Mon 2/10/20	Fri 5/15/20											
687	PG&E Contract Review with EE PRG	6 days	Tue 5/26/20	Tue 6/2/20											
688	PG&E Final Award and Contract Signed	2 days	Tue 7/28/20	Wed 7/29/20											
689	PG&E Submit Advice Letter	9 days	Tue 6/30/20	Fri 7/10/20											
690	PG&E Advice Letter Approved														
691	PG&E Implementation Plan	23 days	Mon 11/9/20	Wed 12/9/20											
692	PG&E - Local Govt. Partner (non-resource programs)	376 days?	Fri 3/22/19	Fri 8/28/20											
693	PG&E RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19											
694	PG&E RFA Release	0 days	Thu 5/23/19	Thu 5/23/19											
695	PG&E RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19											
696	PG&E RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19											
697	PG&E RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19											
698	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19											
699	PG&E RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19											
700	PG&E RFP Release	0 days	Mon 11/4/19	Mon 11/4/19											
701	PG&E RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19											
702	PG&E RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20											
703	PG&E RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20											
704	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20											
705	PG&E Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20											
706	PG&E Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20											
707	PG&E Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20											
708	PG&E Submit Advice Letter		N/A	N/A											
709	PG&E Advice Letter Approved														
710	PG&E Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20											
711	PG&E - SW Codes & Standards (RFP only)	221 days?	Mon 7/8/19	Mon 5/11/20											
712	PG&E RFA Preparation		N/A	N/A											
713	PG&E RFA Release		N/A	N/A											
714	PG&E RFA Abstract Creation Duration		N/A	N/A											
715	PG&E RFA Evaluation		N/A	N/A											
716	PG&E RFA Review with EE PRG		N/A	N/A											
717	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A											
718	PG&E RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19											
719	PG&E RFP Release	1 day	Tue 9/10/19	Tue 9/10/19											
720	PG&E RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19											
721	PG&E RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
722	PG&E RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19											
723	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19											
724	PG&E Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20											
725	PG&E Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20											
726	PG&E Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20											
727	PG&E Submit Advice Letter		N/A	N/A											
728	PG&E Advice Letter Approved														
729	PG&E Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20											
730	PG&E - Local Multi-Sector (40% outsource)	290 days?	Tue 4/28/20	Mon 6/7/21											
731	PG&E RFA Preparation		N/A	N/A											
732	PG&E RFA Release		N/A	N/A											
733	PG&E RFA Abstract Creation Duration		N/A	N/A											
734	PG&E RFA Evaluation		N/A	N/A											
735	PG&E RFA Review with EE PRG		N/A	N/A											
736	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A											
737	PG&E RFP Preparation		N/A	N/A											
738	PG&E RFP Release		N/A	N/A											
739	PG&E RFP Proposal Creation Duration		N/A	N/A											
740	PG&E RFP Evaluation		N/A	N/A											
741	PG&E RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20											
742	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder														
743	PG&E Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20											
744	PG&E Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20											
745	PG&E Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20											
746	PG&E Submit Advice Letter	25 days	Mon 1/4/21	Fri 2/5/21											
747	PG&E Advice Letter Approved														
748	PG&E Implementation Plan	46 days	Mon 4/5/21	Mon 6/7/21											
749	PG&E - SW New Construction	576 days?	Mon 3/25/19	Mon 6/7/21											
750	PG&E RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19											
751	PG&E RFA Release	1 day	Tue 5/28/19	Tue 5/28/19											
752	PG&E RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19											
753	PG&E RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19											
754	PG&E RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19											
755	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19											
756	PG&E RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20											
757	PG&E RFP Release	1 day	Mon 3/16/20	Mon 3/16/20											
758	PG&E RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20											
759	PG&E RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
760	PG&E RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20											
761	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20											
762	PG&E Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20											
763	PG&E Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20											
764	PG&E Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20											
765	PG&E Submit Advice Letter	25 days	Mon 1/4/21	Fri 2/5/21											
766	PG&E Advice Letter Approved														
767	PG&E Implementation Plan	46 days	Mon 4/5/21	Mon 6/7/21											
768	SW WE&T K-12 Connections	357 days?	Tue 1/7/20	Wed 5/19/21											
769	PG&E RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20											
770	PG&E RFA Release	1 day	Mon 4/6/20	Mon 4/6/20											
771	PG&E RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20											
772	PG&E RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20											
773	PG&E RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20											
774	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20											
775	PG&E RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20											
776	PG&E RFP Release	1 day	Fri 9/4/20	Fri 9/4/20											
777	PG&E RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20											
778	PG&E RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20											
779	PG&E RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20											
780	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 11/19/20	Fri 11/20/20											
781	PG&E Contract Negotiation and Development	44 days	Mon 12/7/20	Thu 2/4/21											
782	PG&E Contract Review with EE PRG	6 days	Fri 2/19/21	Fri 2/26/21											
783	PG&E Final Award and Contract Signed	15 days	Fri 2/26/21	Thu 3/18/21											
784	PG&E Submit Advice Letter	2 days	Fri 3/19/21	Mon 3/22/21											
785	PG&E Advice Letter Approved														
786	PG&E Implementation Plan	45 days	Tue 6/1/21	Mon 8/2/21											
787	SW WE&T Career and Workforce Readiness	410 days?	Tue 1/7/20	Mon 8/2/21											
788	PG&E RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20											
789	PG&E RFA Release	1 day	Mon 4/6/20	Mon 4/6/20											
790	PG&E RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20											
791	PG&E RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20											
792	PG&E RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20											
793	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20											
794	PG&E RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20											
795	PG&E RFP Release	1 day	Fri 9/4/20	Fri 9/4/20											
796	PG&E RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20											
797	PG&E RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
798	PG&E RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20											
799	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 11/19/20	Fri 11/20/20											
800	PG&E Contract Negotiation and Development	44 days	Mon 12/7/20	Thu 2/4/21											
801	PG&E Contract Review with EE PRG	6 days	Fri 2/19/21	Fri 2/26/21											
802	PG&E Final Award and Contract Signed	15 days	Fri 2/26/21	Thu 3/18/21											
803	PG&E Submit Advice Letter	2 days	Fri 3/19/21	Mon 3/22/21											
804	PG&E Advice Letter Approved														
805	PG&E Implementation Plan	45 days	Tue 6/1/21	Mon 8/2/21											
806	SW State of California / Dept. of Corrections	348 days?	Sun 3/1/20	Tue 6/29/21											
807	PG&E RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20											
808	PG&E RFA Release	1 day	Wed 5/13/20	Wed 5/13/20											
809	PG&E RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20											
810	PG&E RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20											
811	PG&E RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20											
812	PG&E RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20											
813	PG&E RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20											
814	PG&E RFP Release	1 day	Wed 9/9/20	Wed 9/9/20											
815	PG&E RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20											
816	PG&E RFP Evaluation	16 days	Fri 10/23/20	Fri 11/13/20											
817	PG&E RFP Review with EE PRG	6 days	Tue 11/24/20	Tue 12/1/20											
818	PG&E RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 12/7/20	Fri 12/11/20											
819	PG&E Contract Negotiation and Development	41 days	Fri 12/4/20	Fri 1/29/21											
820	PG&E Contract Review with EE PRG	5 days	Tue 2/23/21	Mon 3/1/21											
821	PG&E Final Award and Contract Signed	15 days	Mon 3/8/21	Fri 3/26/21											
822	PG&E Submit Advice Letter	1 day	Fri 4/30/21	Fri 4/30/21											
823	PG&E Advice Letter Approved														
824	PG&E Implementation Plan	44 days	Thu 5/20/21	Tue 7/20/21											

Project: IOU Master Task Timeli
Date: Wed 10/28/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
